

ISMC221 : IS PROJECT MANAGEMENT  
Final Examination

# Project Management Plan

## **Group 2**

Natividad, Jearevh F.  
Naval, Matthew Cymig F.  
Maravilla, Jeremy M.  
Samson, Kaye V.

**Submitted to**  
Michelle Elija B. Santos

**May 19, 2025**

# Project Management Plan

## Project Overview

- Project Title: Happy Pixies Digital Event Management System
- Project Manager: Jearevh Natividad
- Project Start Date: April 1, 2025
- Project End Date: December 1, 2025

## Project Objectives

This project management plan is designed to develop a digital event management system with the primary goal of providing the following functions:

- Develop a centralized system for managing client bookings and event execution.
- Implement a real-time inventory tracking system for reusable decorations and supplies.
- Improve staff scheduling and assignment through an automated workforce management tool.
- Enhance financial tracking with a digital invoicing and payment management system.
- Integrate digital tools for vendor coordination and logistics planning.
- Ensure the system is mobile-friendly and accessible offline for on-site event management.

## Scope

This project includes the development of features essential to digital event management. The key components of the Happy Pixies Digital Event Management System are client booking and event execution management, along with finance and accounting functionalities such as payments, invoicing, and budgeting. The system will also support staff scheduling and workforce management, as well as inventory and warehouse tracking to manage reusable supplies. Procurement and supplier coordination, logistics and event-day management, and customer relationship management (CRM) will be integral parts of the platform. Additionally, the plan includes

elements of digital transformation, including the integration of tools like Google Workspace and support for online inquiries and contract management.

The project will not include e-commerce functionalities beyond those related to event bookings. It will also exclude the development of a full-scale enterprise resource planning (ERP) system, as well as the implementation of advanced AI-based automated decision-making for event planning.

Work Breakdown Structure




Figure 1: Happy Pixies Digital Event Management System Work Breakdown Structure



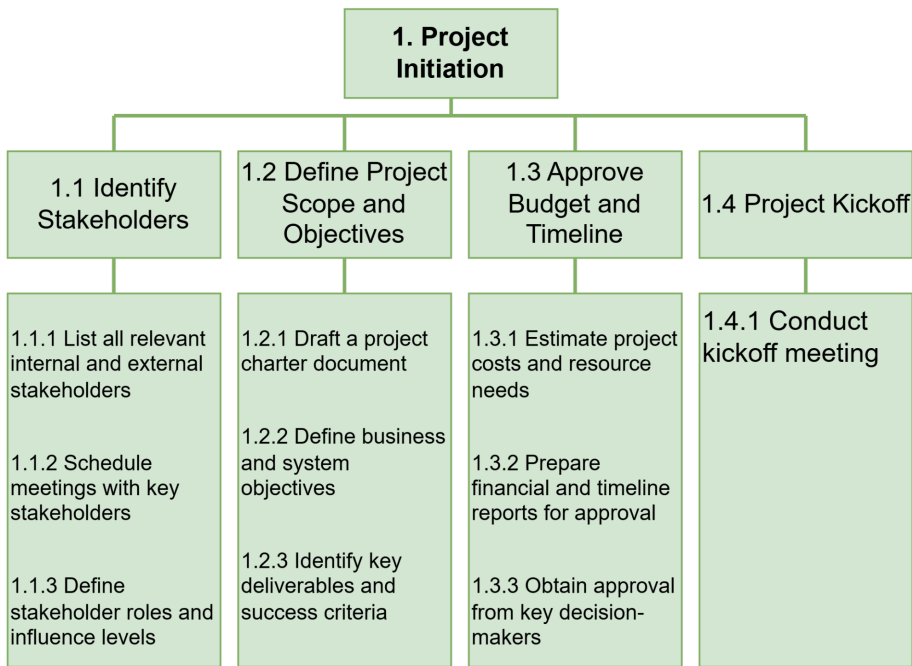



Figure 1.1: Project Initiation (WBS)

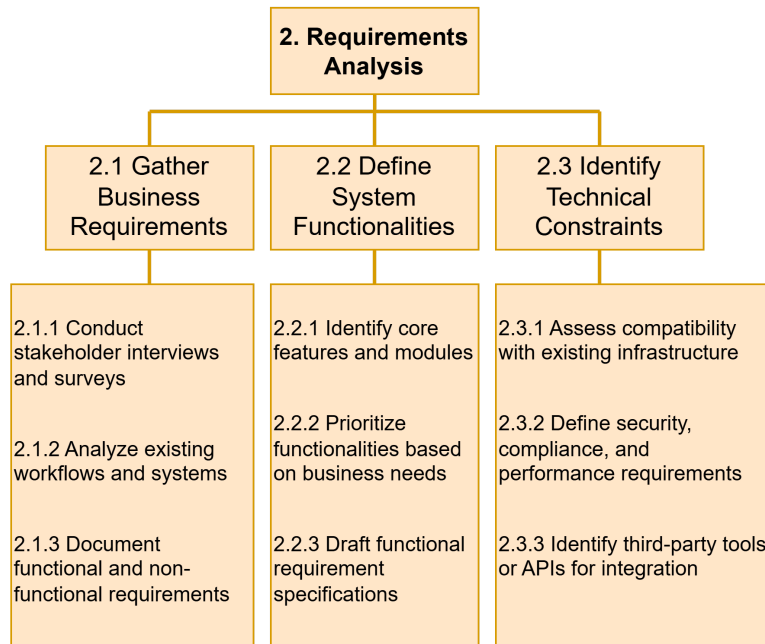


**Figure 1.2: Requirement Analysis (WBS)**

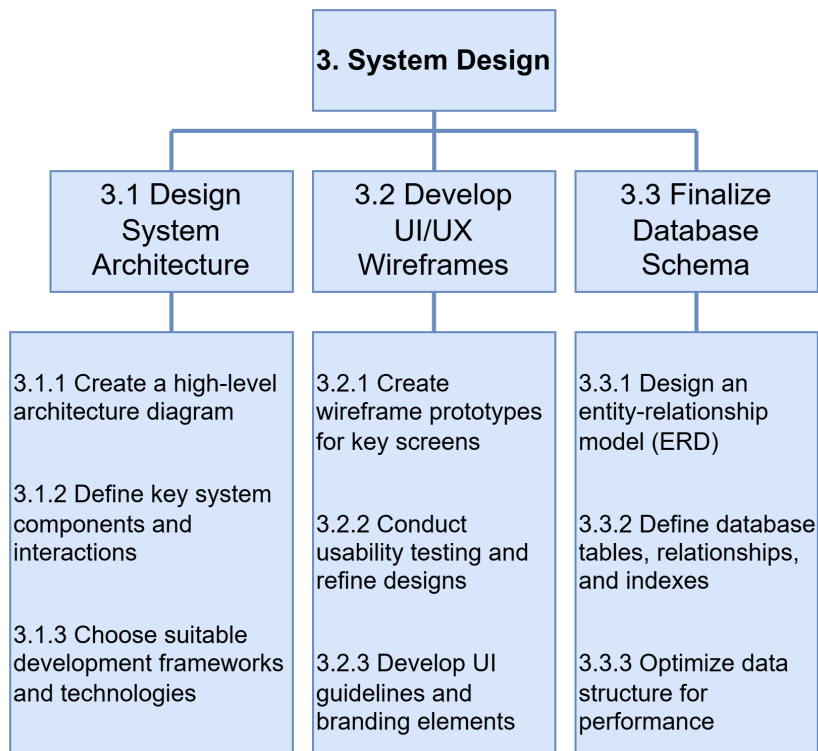


**Figure 1.3: System Design (WBS)**

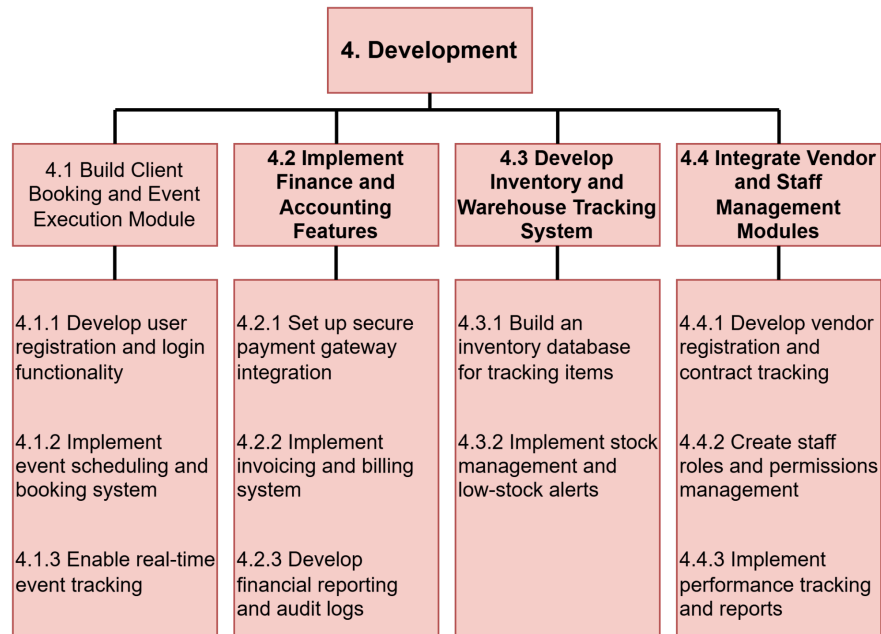


**Figure 1.4: Development (WBS)**

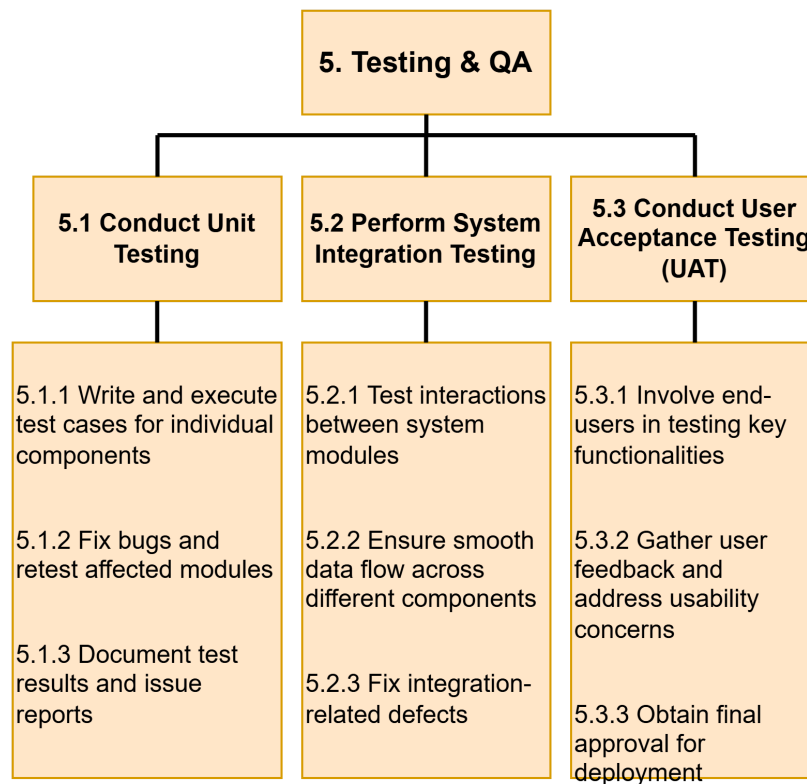

**Figure 1.5: Testing & QA (WBS)**

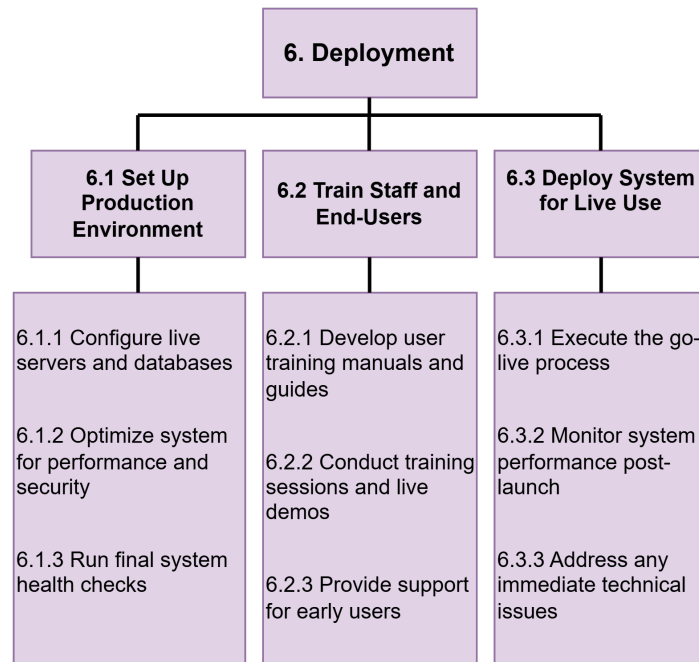

**Figure 1.6: Deployment (WBS)**

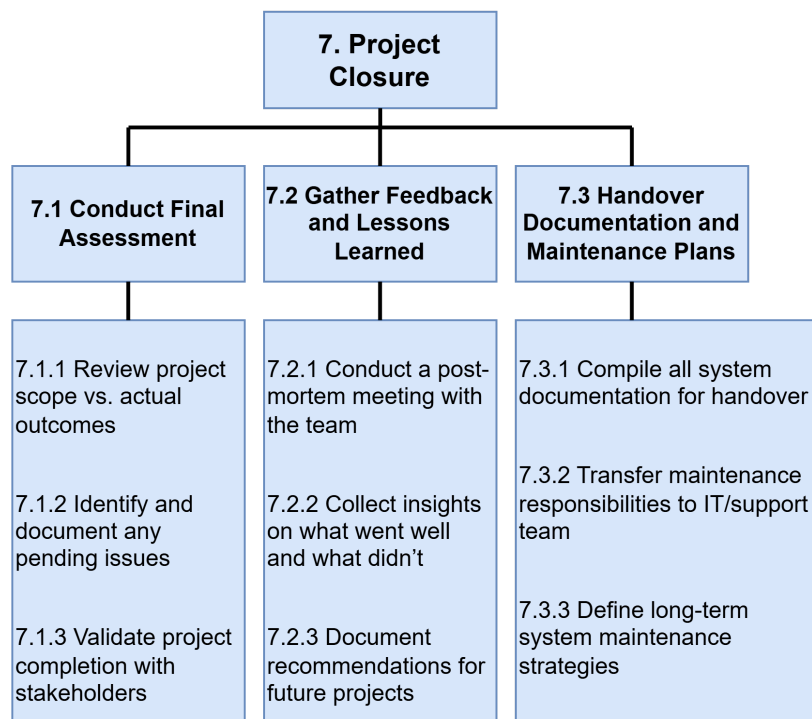

**Figure 1.7: Project Closure (WBS)**

## Deliverables

- Web-based Event Management System (EMS)
- Mobile-friendly interface for on-site management
- Digital contract and invoice generation module
- Real-time inventory tracking system
- Staff scheduling and role assignment tool
- Vendor coordination and logistics module

## Stakeholders

| Name              | Role            | Responsibility                                    |
|-------------------|-----------------|---------------------------------------------------|
| Michael U. Naval  | Co-owner        | Project Sponsor & Business Process Consultant     |
| Jearevh Natividad | Project Manager | Oversee development and implementation            |
| Jeremy Maravilla  | Developer       | System architecture and development               |
| Kaye Samson       | UX/UI Designer  | Interface design and user experience optimization |
| Matthew Naval     | Tester          | System testing and quality assurance              |

# Timeline

| Phase                 | Activities                                                       | Start Date       | End Date           | Duration   | Milestone                       |
|-----------------------|------------------------------------------------------------------|------------------|--------------------|------------|---------------------------------|
| Project Initiation    | Kick-off meeting, stakeholder alignment, team assignments        | April 1, 2025    | April 10, 2025     | 2 weeks    | Project Charter Approved        |
| Requirements Analysis | Gather business requirements, user stories, and functional specs | April 11, 2025   | May 10, 2025       | 1 month    | Requirements Document Finalized |
| System Design         | Create UI mockups, system architecture, and database schema      | May 11, 2025     | June 15, 2025      | 5 weeks    | Design Approved                 |
| Development Phase 1   | Core modules: booking, inventory, scheduling                     | June 16, 2025    | August 15, 2025    | 2 months   | Core Features Developed         |
| Development Phase 2   | Add-on modules: vendor coordination, invoicing, mobile interface | August 16, 2025  | September 30, 2025 | 1.5 months | Full System Ready               |
| Testing & QA          | Unit testing, integration testing, UAT with client               | October 1, 2025  | October 31, 2025   | 1 month    | QA Sign-Off                     |
| Deployment & Training | System launch, user training, documentation handoff              | November 1, 2025 | November 30, 2025  | 1 month    | System Deployed                 |
| Project Closure       | Project evaluation, final report, knowledge transfer             | December 1, 2025 | December 15, 2025  | 2 weeks    | Project Closed                  |



Gantt Chart

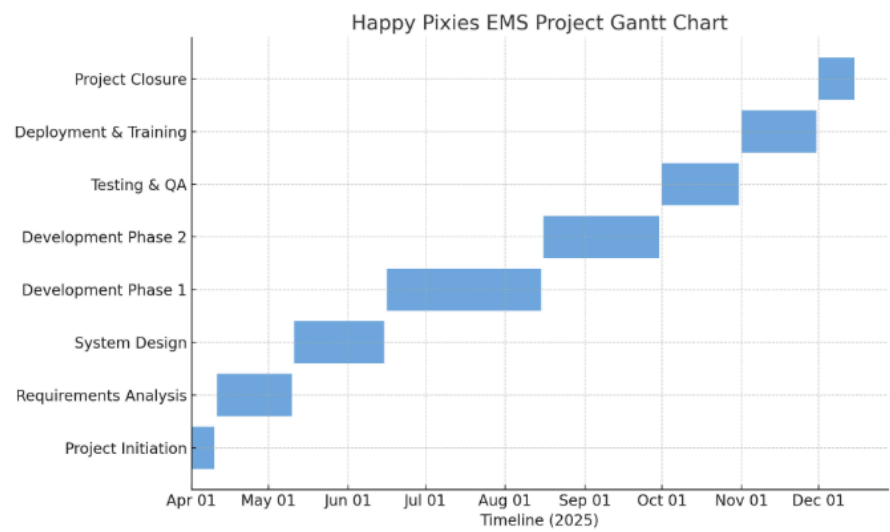


Figure 2: Gantt Chart of Happy Pixies Digital Event Management System

Budget

| Resource                                   | Estimated Cost          |
|--------------------------------------------|-------------------------|
| Software Development (Web & Mobile)        | PHP 500,000 - 1,000,000 |
| Hardware (Servers, Hosting, Cloud)         | PHP 50,000 - 100,000    |
| Personnel (Developers, Designers, Testers) | PHP 300,000 - 600,000   |
| Training (Staff & Users)                   | PHP 50,000              |
| Other Costs (Licensing, Maintenance)       | PHP 100,000             |
| Total Budget                               | PHP 1M - 1.8M           |

## Communication Plan

Effective communication is vital for the success of the Happy Pixies Event Management System. The project team will use various channels and frequencies depending on the stakeholder and project phase.

| Communication Type          | Frequency                                                    | Methods                              | Stakeholders                                               |
|-----------------------------|--------------------------------------------------------------|--------------------------------------|------------------------------------------------------------|
| Internal Team Communication | Weekly stand-up meetings (Every Monday)                      | Google Meet, Slack, Trello           | Developers, Tester, UI/UX Designer, Project Manager        |
| Sponsor Communication       | Bi-weekly updates                                            | Email summaries, video calls         | Project Manager, Project Sponsor                           |
| Client Feedback/Testing     | After major milestones (e.g., Design Approval, Beta Release) | Google Forms, Zoom feedback sessions | Project Sponsor, Client-side staff, UI/UX Designer, Tester |
| Documentation and Reports   | Monthly progress reports                                     | Google Docs shared folder            | Project Sponsor, Project Manager, Team                     |

## Quality Management

To ensure the highest level of quality throughout the development of the Event Management System, the following processes will be implemented:

- **Quality Standards**
  - Adherence to ISO/IEC 25010 Software Quality Standards
  - User satisfaction, system reliability, and mobile responsiveness are key quality indicators
- **Quality Assurance Activities**
  - Regular code reviews using GitHub
  - Design reviews with UX/UI mockups

- Weekly testing sessions led by the QA Tester
- Requirement traceability matrix to ensure all deliverables are met
- **Quality Control Procedures**
  - Automated testing scripts for form validations and data processing
  - Manual testing for usability and UI responsiveness
  - UAT (User Acceptance Testing) in October 2025
- **Documentation**
  - Test cases, bug reports, QA logs maintained using Google Sheets

## Human Resources

Below is an outline of team roles, responsibilities, and skills required:

| Team Member       | Role                         | Responsibilities                                 | Required Skills                      |
|-------------------|------------------------------|--------------------------------------------------|--------------------------------------|
| Jearevh Natividad | Project Manager I, Developer | Oversees project, assigns tasks, writes code     | Leadership, PHP, MySQL               |
| Jeremy Maravilla  | Developer                    | Backend logic and database implementation        | Laravel, MySQL, API integration      |
| Kaye Samson       | UX/UI Designer               | Designs wireframes and final UI                  | Figma, UX principles, responsiveness |
| Matthew Naval     | Tester                       | Conducts QA tests and ensures system reliability | Manual testing, test documentation   |
| Michael Naval     | Sponsor/Advisor              | Approves progress and provides business insights | Business consulting                  |

## Responsibility Assignment Matrix (RAM)

| Task               | Jearevh | Jeremy | Kaye | Matthew | Michael |
|--------------------|---------|--------|------|---------|---------|
| Project Planning   | R       | C      | C    | C       | A       |
| System Development | A       | R      | C    | I       | I       |
| UI/UX Design       | C       | I      | R    | C       | I       |
| Testing            | C       | C      | C    | R       | I       |
| Approval & Review  | I       | I      | I    | I       | A       |

**Legend:** *R* - Responsible, *A* - Accountable, *C* - Consulted, *I* - Informed

## Risks

### Risk Management Process

1. **Risk Identification** – Conducted during planning and design stages.
2. **Risk Analysis** – Assess likelihood and impact.
3. **Risk Mitigation Planning** – Define actions to reduce or eliminate risk.
4. **Monitoring and Review** – Weekly updates and risk status review

### Risk Assessment Matrix

| Risk                               | Probability | Impact | Mitigation Strategy                                   |
|------------------------------------|-------------|--------|-------------------------------------------------------|
| Staff resistance to the new system | Medium      | High   | Conduct orientation and involve them in testing       |
| Data migration issues              | High        | High   | Validate data early and use data templates            |
| Technical bugs in deployment       | Medium      | High   | Conduct thorough testing and phased rollout           |
| Internet downtime during events    | High        | Medium | Ensure offline access is available                    |
| Budget overrun                     | Low         | High   | Maintain contingency fund and regular budget tracking |

# Closure

The closure phase will ensure the project is formally finalized and evaluated:

- **Final Deliverables**
  - Fully functional EMS (web and mobile)
  - Documentation (user manual, developer guide)
  - Final QA reports and testing results
- **Client Acceptance**
  - Final demonstration and sign-off by the Project Sponsor
- **Post-Implementation Review**
  - A retrospective meeting to evaluate successes, failures, and lessons learned
- **Project Archive**
  - All documentation, code, and reports will be stored in a shared Google Drive folder accessible to the sponsor and team
- **Transition to Maintenance**
  - Assign a point-of-contact for ongoing support and prepare a knowledge transfer session with the client's staff

# Approval

By signing this document, the following individuals acknowledge and approve the project.

**Project Sponsor:**

Michael U. Naval  
Co-owner, Happy Pixies  
[Signature]  
3/29/25

**Project Manager:**

Jearevh Natividad  
Project Manager  
[Signature]  
3/29/25

**Subject Adviser:**

Michelle Elijah Santos  
Subject Adviser, Project Management  
[Signature]  
3/29/25
